



KU Cultural Week: Annual Cultural Exchange

Group 8

Dagmar Bojesen | Om Vaknalli | Blaleyminh Stéphanie-Aimée Mé | Smilla Huzell
bst465 pkv263 fhj591 kcb103

LFFK10278U Project Management – Faculty of Sciences
2025

Table of Contents

1. Status report	3
2. Introduction and Team Establishment	4
3. Project proposal	14
4. Project Charter	15
5. Project analysis	19
6. Project plan	32
7. Learning reflection	42

1. Status report

KU Cultural week: Annual cultural exchange

How amazing would it be for internationals to familiarise themselves with Danish culture and vice versa?! KU’s student and staff population is a microcosm of the cultural diversity which exists in Copenhagen. KU’s cultural week aims to leverage this vast culture to create an opportunity for all students and staff to socialise around food, performances, discussions, and other activities.

Key activities for the last period	Key activities for next period
• Core team formation • Finalisation of event idea and activities • Determination of goal hierarchy • Definition of WBS and network diagram • Establishment of budget	• Securing administrative permits and venues • Securing funding from internal and external sources • Recruitment of volunteers • Training of volunteers • Launching marketing strategy including student sign-ups for event
Risks	Risk management
• No volunteers sign up for the event • No available rooms for the team or volunteers’ meetings • The organisation team does not receive an accurate approximation of attendees for the event. • The project does not receive at least 50% feedback from the event.	• Change the volunteering position to a paid position. • Host all meetings online (teams/zoom etc.) whereby all attendees can join from home. • Keep planning the event for the expectant 300 attendees as set up in goal. • Wait and see. Further make an internal assessment of the event.

Note: all text in red in the rest of the document represent an update made to the team’s initial thoughts about teamwork or an aspect of the project.



2. Introduction and Team Establishment

2.1. Presentation of team

Dagmar Bojesen

Dagmar Bojesen, studying Msc Food science and technology the general profile. A Danish student coming from Århus, with an interest in science and motivating people to grow in their abilities. Dagmar wants to strengthen analytical and structural skills in leading a project.



Om Vaknalli

Om Vaknalli is pursuing his Erasmus Mundus Joint Masters Degree in the field of sustainable forest & nature management at the University of Copenhagen. With a background in earth and environmental sciences, he hopes to lead projects in ecology, biodiversity management and sustainable living, more specifically to plan the study of permacultural practices in green Danish societies during the next block.



Stéphanie Mé

Stéphanie Mé is on a full-time student at KU, studying a Msc in Agricultural Economics. Stéphanie is originally from Côte d'Ivoire, where she worked for an international development consultancy firm focusing on public policy advisory in agricultural value chains and technology. She is keen to use this experience to enrich her project management toolbox, as well as contribute with her structured problem-solving skills to create a realistic and implementable project.



Smilla Huzell

Smilla Huzell is a guest student from CBS in the Masters in Business Administration and Bioentrepreneurship. Originally from Sweden, Smilla has an international background and believes true progress comes from interdisciplinary and cross-cultural diversity. With a BSc. in Biochemistry and three years in early start up developments, Smilla now hopes to use her unique toolbox and experiences to develop her project management skills in planning high impact events.



2.2. Ground Rules and guides for meetings and log file

The following statements provide the guidelines for the ground rules for operation within the team. Clarifications for valuation is provided where necessary to further align the team on overall message.

- 1) It is important to formulate rules about meetings: when to meet, where to meet, what kind of meetings, preparations for meetings, recording of meetings and cancellations.

Agrees - **1**-----2-----3-----4-----5 - Disagrees

Comment: N/A

- 2) Decisions in the group are made by the majority.

Agrees -1-----2-----**3**-----4-----5 - Disagrees

Comment: The project manager has the final decision based on the group discussion

- 3) There is zero tolerance for bullying a way through a problem or an issue.

Agrees - **1**-----2-----3-----4-----5 - Disagrees

Comment: N/A

- 4) There should be allotted time at the group meetings for chats about stuff that does not have anything to do with the project as well as time for drinking coffee and eating cake.

Agrees - **1**-----2-----3-----4-----5 - Disagrees

Comment: When time allows to foster a trusting environment.

- 5) All members of the group are expected to contribute with the same amount of work in the project work.

Agrees - 1-----**2**-----3-----4-----5 - Disagrees

Comment: Different tasks require varying degrees of time, as such tasks are delegated and performed as expected from the team.

- 6) It is important to maintain confidentiality; no information is shared outside the group unless all agree to it.

Agrees - 1-----**2**-----3-----4-----5 - Disagrees

Comment: Unless explicitly confidential, external output can be helpful.

- 7) It is the supervisors/teacher's responsibility and task to direct, steer and lead the group and secure that everybody learns what they are supposed to learn.

Agrees - 1-----2-----3-----4-----**5** - Disagrees

Comment: Teachers only responsible for guidance

- 8) Those group members who talk most must control themselves and put a lid on.

Agrees - 1-----2-----**3**-----4-----5 - Disagrees

Comment: This is self-driven with team awareness with feedback.

- 9) An agenda has to be made ready before each meeting in the group.

Agrees - **1**-----2-----3-----4-----5 - Disagrees

Comment: N/A

- 10) Each member of the group is only responsible for one's own learning. What ever the other members might learn is up to them.

Agrees - 1-----2-----3-----4-----**5** - Disagrees

Comment: This is a platform is for feedback and mutual growth.

- 11) The best way to learn about cooperation and working together in a group is when there is an open discussion about each member's role and function.

Agrees - **1**-----2-----3-----4-----5 - Disagrees

Comment: N/A

- 12) It is just as important to discuss feelings as it is to discuss content and factual matters

Agrees - 1-----2-----3-----4-----5 - Disagrees

Comment: Acknowledge feelings top work with them and circumvent any issues.

- 13) Every meeting should be finished off with a short evaluation in which the group reflects on the meeting and whether everything that was planned actually got covered well enough.

Agrees - 1-----2-----3-----4-----5 - Disagrees

Comment: Project Manager evaluates the meetings overall at the end of term. The logfile should contain the meeting minutes and the evaluation.

- 14) The group must keep a log file to be able to keep track of all the important decisions and discussions

Agrees - 1-----2-----3-----4-----5 - Disagrees

Comment: N/A

Conclusion

To compete these ground rules the team individually graded each point to then discuss in plenum. In cases of total agreement, no comment was given as the grading was intuitively unanimous and no clarification on the grading was needed. In cases of differing opinion, discussions were held in order to clarify what the points meant to each team member and commenting on the grading with either additional caveats to the rules or helpful guides.

As an initially sociable groups the points referring to discussions, structure and timings are of importance to be able to complete the whole project in a timely manner. The ground rules essentially provide the team with a baseline framework for respect within the team and to allow for the project manager to manage the team expectations throughout the project.

In week 4, upon realising that the group work was taking longer than expected on several occasions, the ground rules were revisited and reclarified. This was further prompted as self-reflection by individual team members after meetings led to discussions on how different personality types need to be both reigned in or encouraged in different types of group work. Points 2, 3, 4, 8, 9, 11 were discussed and clarified to both streamline the workflows in respect to timings as well as team dynamics with different personality type tendencies.

2.3. Working together

The project manager is expected to provide an agenda before each session considering any lectures being held and necessary project deliverables that need to be discussed and competed. At the end of each session, the Project Manager can delegate any remaining tasks to the group members to complete before the next session. Any action points should be conveyed in writing in the communication channels created (WhatsApp) to ensure that all group members know what is expected of them. All work should be completed and shared in the OneDrive folder created for this specific project. The project manager is responsible for the overall evaluation of the meetings throughout their term whilst team members reflect on the project managers approach to their leadership during their term.

Throughout the project the internal communications worked seamlessly, and the team has been able to work hybrid with some members not being present during class activities. Each PM was also able to provide agendas for each session. More individual action points were delegated towards the end of the project to ensure project completion.

2.4. Learning goals for the team and individually learning goals

Team goals

- Developing time management skills (measured through meeting minutes, keeping to time, getting deliverables ready day before deadline)
- Learn how to constructively work in a group with differing personality traits and how to manage the differing in opinions
- Effectively manage any conflicts arising in the group assignment.
- Develop critical and structural thinking that can be leveraged in a professional setting and deliverables (documentation and argumentation).

Individual learning goals

Dagmar

- Becoming clearer and more precise in my decision making in a team
- Trusting my own intuition more and stand by it
- Train my structural skills, to manage time and to plan a project

Om

- Management and consensus of individual and team expectations from me
- Delivering consistent proactive incremental work output
- Mindfully separating the people from the problem without compromising the efficiency of work
- Pinpointedly locating my excellence as an operating stakeholder in a niche project profile
- Getting comfortable with social interactions at a professional level with different personality types. This also includes taking a lead at proactively speaking out thoughts during group discussions.
- Mindfully developing streamlined project goals that can be attained within the time and resource constraints of the project
- As a PM, producing decisive actions and working on the interpersonal leadership qualities

Stéphanie

- Appropriate the project management tools and frameworks such that there is a concrete justification for signalling, to employers, PM as a hard skill of mine
- Improve planning skills
- Be aware of how my personality type interacts with others and effectively use that for future teamwork

Smilla

- Develop active listening skills by not talking first and taking other perspectives into account before sharing my ideas.
- Let go of control and not micromanage tasks when they are not delegated to me.
- Take more time with decisions to think them through thoroughly.

2.5. The team ambitions

- Have a constructive team work as evidence through structured meetings and feedback.
- Appropriate the project management skills within the limits of the time constraints of the course.
- Produce a quality and realistic project which could potentially be implemented.

2.6. JTI-test: effect and significance for the team

Member	JTI result	Theoretical Description	Comment (<i>is that theoretical desc. accurate for you; what do you think would be the significance for the team?</i>)
Dagmar	ENFP	Campaigner personality type: Independent and creative, tend to embrace big ideas and actions that reflect their sense of hope and goodwill toward others. Their vibrant energy can flow in many directions (NF) Attention to concepts, meaning, interrelationships, and probable or possible futures with a focus on the people and values involved. A growth and development approach	I do not work in a structured way, but where my energy and ideas come to, meaning I sometimes will work on different topics at the same time. I have a very creative mind and gets a 1000 of ideas but can be difficult for me to collect them. I am good at just beginning to write/work, and I need to force structure on myself.
Om	INTP	“Logician” Personality Type: Often described as analytical, inquisitive and intellectually inclined. Typical personality traits include hyperfocus on projects that interest them, thinking without a practical perspective, a strong preference to solo working strategies (except when working with like-minded people), enjoying the freedom of loose organisational structures, thinking big picture and/or outside the box and thinking before speaking/acting.	I agree with most of the traits described by the logician personality type. In addition, I must keep in mind that feelings and values of yourself and others share an equal slice of the pie along with logic and rational thinking, thus appearing sensitive in the bargain by acknowledging the human and emotional sides of people and arguments. Also, I recognise that as per my personality type, I have a low social battery and must make proactive efforts in getting used to small talk. It would help a stronger team dynamic if I can handle criticism better as well as be open to persuasion. Lastly, overcoming my self-doubt can bring forth an exceptional leadership profile.
Stéphanie	ISFJ	“Duty calls” type: Loyal, reliable and considerate people. They have a firm grasp of realities and facts, are observant of detail and have a keen eye for other people’s needs	I have discovered overtime, in personal and professional settings, that I feel more comfortable and can serve better when the environment is structured. Hence, I agree with the “diagnosis” that my associated

		and feelings. They take it upon themselves to do something when they see it as useful and helpful, and most often quietly and behind the scenes. Tend to like stability, structure and tradition which could be perceived as overly conservative. As a leader or manager: often not very motivated to lead but will lead if urged to do so; conscientious about doing things according to accepted values and principles; recognises practical results while insisting on getting details right. Could benefit from: practising a little more boldness and self-assertion; opening to new ideas and experiences; envisioning positive possibilities in for the future; communicating more directly and up-front, also regarding own needs and interests.	personality type likes stability and structure. While I understand the importance of feelings and “coming-from-ness” of people around me, I would tend to prioritise facts also because I see them as necessary to understand the situation. I wouldn’t say that I lack “motivation” to lead but rather I could sometimes “avoid” it because I question my ability to do it properly. However, when I observe lack of structure in an environment or I identify a more helpful way to do something, I just suggest it and provide arguments on why it would be more useful for the advancement of the common good. At this point, I ignore the usual doubts because then, it’s not about me. I disagree with the points on what this type could benefit from because I disagree with the implicit assumption that I am not already doing that. On all points, I do not really recognise my current self. On the contrary, I received positive/negative feedback on my envisioning of positive possibilities, for example. Overall, the team would benefit from structured suggestions and frameworks, push for quality product, down to the detail, push for reflective discussions.
Smilla	ESTJ	Practical, logical and energetic person with a talent for organisation, planning and aggressive decisiveness. Deals with facts and past experiences and is not easily swayed unless convinced by logical arguments based on fact. Responsible, effective and foresighted regarding tasks and is sensible and realistic in most contexts. Motivated to lead and takes charge quickly to make decisions fast adapting previous experience.	I benefit from structure and delegated tasks in teams. Discussions are a fantastic way to work together but ultimately decisions need to be made and acted upon. I enjoy work and will often say yes to any task handed to me but also run the risk of getting overwhelmed. I work great with overarching concepts and the wider implications of the work at hand but will not think about smaller details.

Table 1 – JTI test

2.7. Adapting team knowledge to teamwork

Dagmar

- **Generating and structuring ideas:** I always get a lot of ideas and can think outside the box when it comes to plan a project, but it takes me some time to get a structure on it or a clear vision. This often happens together with others, as I need to speak my ideas and thoughts out loud to process them properly.
- **Passion and potential impatience:** I can easily get carried away in a conversation, no matter if it is about private or personal matters, because I enjoy learning more about the people around me. This can be a problem, as it takes time away from the actual work that needs to be done. I think it come from a natural curiosity, and therefore I don't shy away from a discussion with disagreements either. I tend to be very patient, but if I really care about something, then I can become more dominating, stepping my ground where my impatient side will show up.
- **Structure and timeliness:** I really enjoy teamwork and like to jump around with different tasks, and help were needed, but it can seem very unstructured for others, the way I tend to work, as it is very energy driven, about what I feel inspired to work on. But that said, it is very important to me to do my tasks on time.

Om

- **Individual work:** Whenever possible, I prefer to think aloud and therefore work alone.
- **Time awareness and task prioritisation:** Due to my Adult ADD, I often misjudge the amount of time a certain task takes. It also affects my judgement of prioritisation of tasks as per importance. As a result, I often hold out on completing important tasks until very close to the deadline. Hence, a more conservative deadline (individually or as a team) is helpful in keeping the individual and team stress under check.
- **Potential mischaracterisation of perspectives:** I like to present my arguments in a rational and logical manner. In the bargain, they are often mis-portrayed as insensitive or impersonal. I would not mind if the PM or other group members acknowledge this and probe into deeper clarifications about the argument at hand if they feel the same.
- **Introversion:** I am an introvert by nature. As a result, I often lack self-confidence in voicing my opinions during group discussions. If such an insufficiency in participation is noticed, the PM could periodically push me to be more active during discussions. This also applies during off-working hours.

Stéphanie

- **Individual reflection:** I need time to reflect on my own sometimes, especially when the material is something I haven't thought of before, otherwise my "off-the-cuff" contributions might not be the best or I would just not speak. This doesn't imply that I don't like group discussions, quite the opposite, actually.
- **Group learning and time implications:** Following up on previous point, I would tend to value group learning a lot so I could push for us to do a lot of the activities together or at least for us to discuss together after individual completion of the tasks. The idea would be to see how everyone thinks about it such that we can

each learn. This could sometimes result in me stretching out conversations and not knowing how to end them (risk for time constraints).

- **Structure and frameworks:** I like to spend time on structure and frameworks of how to go about a task before starting it out. I believe freestyling still has a place but, after structure, especially when we have deadlines. I have received feedback from previous groups that it could be a bit rigid but I'm open to discussion on it.
- **Disagreements:** I don't have an issue with disagreements; I tend to perceive them as a good opportunity for discussion, so I'd probably open it up with: "oh that's interesting, I have a completely different opinion/I disagree". And I would tend to detach emotions from the discussion and prioritise the facts about it in order to analyse it. This could seem insensitive (from some feedback I've received) but it's never malicious so just ask if something is unclear.
- **Assertiveness:** I have a hard time categorising myself in one personality type so it could maybe feel like I'm not positioning myself anywhere specifically. It could be difficult to know where to put me. That's an impression I have, I'm still trying to understand/investigate that in me.

Smilla

- **Structure:** I appreciate structure and am more than happy to help the team stay on task and on time acting as secretary or time manager. Furthermore, I can help in creating and formatting any of the documentation.
- **Clarity in action points:** I enjoy discussions of ideas but need a clear action plan and action points for each member to work. As such I thrive with a balance of discussions and own work to deliver on our project.
- **Open communication:** If any issues arise, I would like open communication lines to be available. Each member should be free to express their constructive feedback. A risk with my personality type is that I will take over tasks, please feel free to stop me from doing so.

To conclude, the following are strategies that the project manager can employ for the group work to run seamlessly:

1. Group Discussions

- The team agree that open discussions need to be held to come to consensus on tasks and decisions.

2. Clear Schedule of Tasks

- Each member of the team points out a need for structure whether that be to improve their work or as a proviso for being able to do their best work. Thus, a schedule or agenda should be sent out to the team in order to prepare for the upcoming work.

3. Time for clarification / disagreements

- Whilst discussions are held, the project manager must ensure that the entire team is on the same page. As such, the project manager must ensure that there is time on the schedule for questions and clarifications for the team or to solve any lingering disagreements in the team.

4. Clear Communication

- The project manager should employ clear lines of communication and platforms for group work to facilitate collaborative work. Furthermore, the

project manager should be able to step in and facilitate in situations where miscommunication has occurred within the team.

5. Allotted time for idle chit chat

- Upon reflection in week 4 regarding time management, the project manager must also be able to keep an eye on the time allotted for idle chit chat versus group discussions. This is to ensure that all necessary work is done.

6. Individual Work

- Utilised in the last week, The project manager should be able to delegate tasks to team members to work on individually to complete deliverables to a desired quality.

Throughout the project, both the ground rules and ways of working together were revisited and refined to streamline the workflow and clarify how we wanted to work as a team.

2.8. Situational leadership

In the beginning phase, the forming phase, the team members had to get to know each other and feel comfortable working together, creating a trusting environment. It was done through teambuilding exercises to make people connect and laugh. This created a foundation to talk about the expectations for the project and how to divide the roles and responsibilities during the project in the storming stage. The approach to the team organisation was very much a flat structure, hence with the PM exhibiting more participating and delegating leadership styles. The delegation was focused on the team members' needs and leveraging their unique skillsets appropriately depending on the tasks. Even though the flat working structure created a comfortable space for working, there was, at times, an impact of time management. In these cases, the PM adopted a more directive behaviour to ensure the project was back on track.

The team agreed on common goals related to active participation in teamwork, improvement of management skills, and the respect of the PM's authority as the primary facilitator and as having the tiebreaking vote in case of disagreements.

When agreeing on the ground rules through the norming stage, a supportive behaviour in the leadership was important, such that all felt secure and heard, in order to reach an alignment on the work approach expectations.

In the performing stage, where the actual project work began, the telling and delegating leadership styles became more apparent, as the PM delegated out the tasks required for project advancement and where necessary, directed how they could be done. This was done both during the meetings and through minutes shared afterwards. While this provided clarity and push for quality in achieving tasks, it also clashed with other leadership style preferences within the team.

However, as per the ground rules, the PM was still in charge of structuring the work and facilitating discussions within the team, to which the team members were receptive, evidenced by their eagerness to participate take on tasks.

2.9. Different aspects that are important for the Project Manager to know about the team

- **Communication**

The team is very communicative and will need proper channels to convey information. The communication also needs to be managed so that discussions stay on point and do not go off on tangents.

- **Time Management**

The team will need to be managed in terms of timings when performing tasks. As a discussive team, there is a risk of going overtime. As such the project manager should be mindful of how long tasks are taking to not fall behind. Furthermore, as there is a lot of work to be done, the project manager should allow for breaks and energisers in order to motivate the team throughout the project.

- **Delegating Tasks**

Each team member can work independently as well as within the group. The project manager should, when possible, be able to give individual tasks after group discussions to complete the project on time.

- **Personality Traits and Roles**

The team is aware of their own personality types and the project manager should encourage reflection on how personality traits are affecting the overall group work. These reflective discussions can be used to check in with the team ensuring that each member is learning and growing throughout the project.

3. Project proposal

3.1. Title

A yearly event.

3.2. Goal

Provide a platform to increase cultural awareness and exchange at KU ran by student volunteers.

3.3. Problem to solve

No or limited marketed events for cultural exchange at KU.

3.4. Deliverables

The key components to achieve a successful event are as follows:

- A core organising team
- A schedule for the event
- An admin "green light"
- Volunteers
- Booths and equipment
- A 3-day event
- Participant feedback

3.5. Target group

KU students and staff.

3.6. Impact of not doing project

(i) Lack of cultural integration at KU, (ii) limited university social life, (iii) KU “misses” out on the possibility to improve its image.

3.7. Timeframe

6 months. * 9 months (see network diagram)

3.8. Purpose of initiation

It is an idea for the improvement of the students’ social life that can be transformed into a recurring event. It is also an opportunity to reinforce the identity of the university as being a hub for international cultures in Copenhagen.

3.9. Primary purpose

Socioeconomic – not for profit but rather for community building.

3.10. Secondary purpose

Reputation (which could lead to sales growth), and/or competence development.

3.11. Make short argument

The purpose of the event is to create a better social life at campus and to engage international students with Danish students to create more cultural exchange at campus. By fostering cross-cultural friendships, the event can contribute to a more inclusive atmosphere and help international students feel more connected to KU. In the long term, this initiative could enhance KU’s reputation as a globally minded university, attracting more exchange students and enriching campus diversity.

4. Project Charter

Project title: Annual Cultural Exchange

Overall Project Goal

To facilitate an annual cultural exchange at Copenhagen University for students and staff.

4.1. Background and Justification

While Copenhagen University (KU) is home to a diverse international community, it has been observed that there is a limited number of marketed events for international cultural exchanges on campus. Hence, an annual event would be an ideal platform to increase this cultural awareness and exchange within KU. Furthermore, allowing the event to be run by student volunteers will create a sense of ownership and an additional opportunity for a cultural exchange amongst them.

The event would provide socioeconomic benefits through a potential increase in student satisfaction. This will be done specifically by enriching students' social life through providing them with options for more activities and thereby improving their experience at the university.

Moreover, the event would contribute to improving the university's reputation, with regards to its active catering to its international community, as well as its commitment to providing volunteering opportunities to students.

4.2. Goal Hierarchy

The main goal of the project is to facilitate an annual cultural exchange at KU for students and staff. This goal has been further categorised into "the organisation" and "the event" sub-categories with an idea to ensure that the team's action clearly accounts for crucial pre-event, during event, and post-event activities. These are laid out in the figure below.

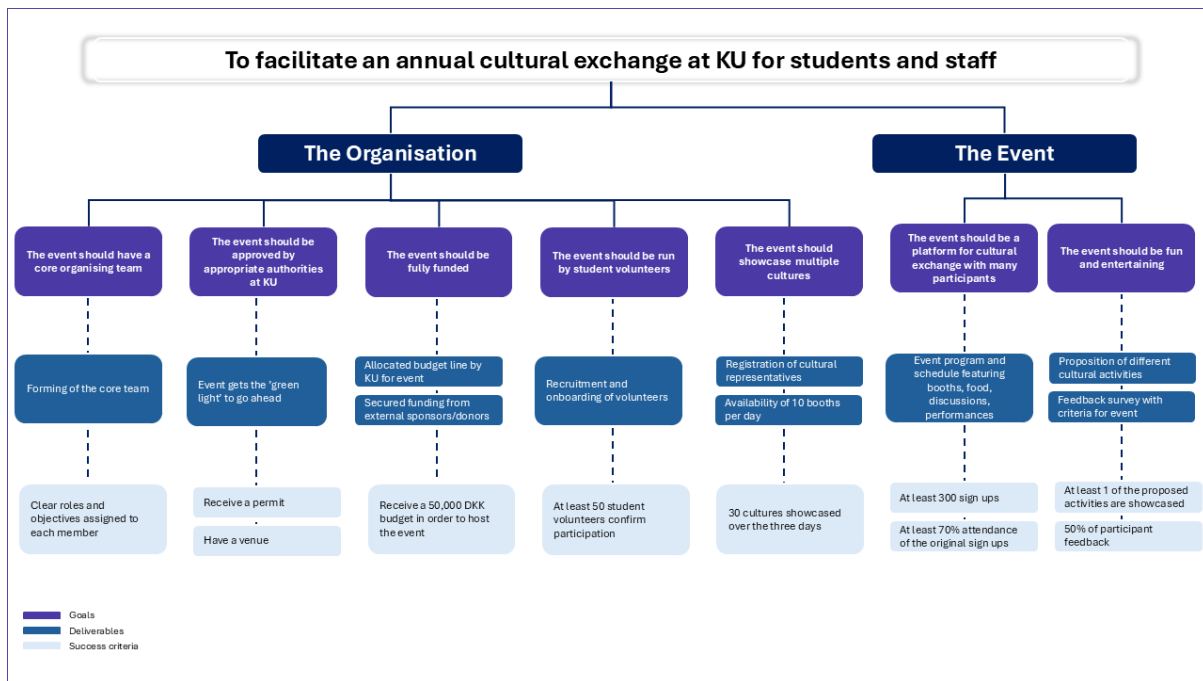


Figure 1 – Goal hierarchy

4.3. Scope Statement

4.3.1. The project delivers:

A 3-day event for cultural exchange providing the venue and facilities with capacity to host 10 booths for representatives and a performance space. The project will be a student volunteer led event with two teams, cultural representative volunteers and organisational volunteers. The project organisers will facilitate by sourcing a 50 000 DKK budget to help cultural representatives procure necessary material for food and/or entertainment. The project will also oversee the marketing and the scheduling of the event.

4.3.2. The project does not deliver:

The project will not be sourcing the cultural items (food, clothes, sport items, performers). This is to be provided by the cultural volunteers and any costs associated will be reimbursed by the project within the 50 000 DKK budget.

4.4. Constraints

The KU festival is on the 25th of May and this project should not compete for space or participants. As such this event should be before this (anywhere from 1 week before to 1 month before).

Upon reflection of dates, the event should be held on the 6th to the 8th of May.

4.5. Assumptions

The following points are assumptions that have been considered for the project planning:

- The project will receive the full 50 000 DKK funding for the event.
- The students would like to volunteer and facilitate this event.

- There will be representatives from 30 cultures (students and staff) during the event days that would like to showcase their cultures.
- A successful marketing strategy has been employed to attract students from across the KU faculties to participate in the event.

4.6. Organisation

4.6.1. Project Owner

The project owner will be Mr. Andreas Blohm Graversen, the Deputy Director at the department of innovation and external partnerships, positioned under the central administration at the University of Copenhagen.

4.6.2. Steering Group

The committee will comprise of the deputy director, administrative officers, and official consultants from the department of innovation and external partnerships.

4.6.3. Project Manager

There will be a collective of four people that will equally hold the title of project manager for this project. They are as follow; Ms. Dagmar Bojesen, Mr. Om Vaknalli, Ms. Stéphanie Mé, and Ms. Smilla Huzell.

4.6.4. Project Core Team

The core team broadly comprises of the following sub-divisions:

- Planning Team - the four project managers and an expert consultant in event management.
- Operations Team - a non-financial resources manager, executing volunteers and key representative members of the student volunteer body in charge of each cultural division.
- Administrative Team: a project coordinator, a representative of the steering committee.
- Financial Team: a representative of the project sponsors and a treasurer

The final agreement on sub-divisions/committees within the core team is:

- Venue team – a person in charge of all securing all venues and facilities.
- Funding team – a person in charge of liaising with internal and external funding partners.
- Volunteer team – two people in charge of the cultural volunteers and a marketing team respectively.

4.6.5. Other Resources and Competences Required

A non-exhaustive list of resources will include sports equipment, musical instruments, stage props, art supplies and souvenirs.

A non-exhaustive list of competencies will include a marketing designer, stall organiser, lighting manager, acoustics manager, social media and outreach manager, **anchor(s)**

for the event, photo & videographers, sports referees, team of first responders, security officials and cultural volunteers.

Upon reflection during work breakdown structure, the team decided that all “specialised” competencies can be completed and performed by volunteers in their respective duties.

4.7. Probability of Success and Risks

To ensure a successful event, several factors need to be accounted for such as the funding to create the event, and enough volunteers to run the event and showcase the different cultures and traditions.

4.7.1. Probability of success

- Receiving the 50.000 DKK funding
- Securing an appropriate venue fitted for 300 participants.
- Creating a cultural exchange between students studying abroad at KU and Danish students to facilitate a better social life at KU.
- A success criterion will be to showcase 30 different cultures within the three days of the event.
- That the event will be a fun experience for the volunteers and participants alike such that it can become a standing annual event.

4.7.2. Risks

- Not receiving the funding to have the event go ahead.
- That students will not volunteer to be a part of the event.
- That people would not like to participate in the event.
- Not gathering sufficient feedback to evaluate the impact of the event.

4.8. Additional Information

No comment at current stage.

5. Project analysis

5.1. SWOT analysis

5.1.1. Positive/Negative elements

POSITIVES	NEGATIVES
1. International campus/community 2. Diverse cultures 3. Various funding avenues (Novo Nordisk) 4. Interest from University (reputation building) 5. KU does run big events already 6. Infrastructure available 7. Large student body 8. Feeding on Copenhagen trendiness: food culture, fashion, metropolitanism 9. Improvement in social life/student life 10. Increasing inter-campus relation	1. Funding unavailability due to dependence on internal funding 2. Marketing outreach due to size of campuses 3. Space limitation 4. Dependence on student volunteering 5. Potential students dis-interest in participation 6. Funding unavailability from external investors 7. Dietary requirements 8. Casualties during the event (injuries from performances, fires)

Table 2 – Positive/Negative elements of project

5.1.2. Positives and negatives categorised as internal or external factors

	POSITIVES	NEGATIVES
INTERNAL	Strengths 11. International campus/community 12. Diverse cultures 13. Various funding avenues (Novo Nordisk) 14. Interest from University (reputation building) 15. KU does run big events already 16. Infrastructure available	Weaknesses 9. Funding unavailability due to dependence on internal funding 10. Marketing outreach due to size of campuses 11. Space limitation 12. Dependence on student volunteering
	Opportunities 1. Large student body 2. Feeding on Copenhagen trendiness: food culture, fashion, metropolitanism 3. Improvement in social life/student life 4. Increasing inter-campus relation	Threats 1. Potential students dis-interest in participation 2. Funding unavailability from external investors 3. Dietary requirements 4. Casualties during the event (injuries from performances, fires)

Table 3 – Positive/Negative elements of project categorised as internal or external factors

5.1.3. Matrix showing strategy and development (Strengths/Weaknesses, Opportunities/Threats)

	Strengths 1. Large student body and international campus/community & Diverse cultures 2. Various funding avenues (Novo Nordisk) 3. Interest from University (reputation building) 4. KU does run big events already / Infrastructure available	Weaknesses 1. Funding unavailability due to dependence on internal funding 2. Difficulty in marketing outreach due to size of campuses 3. Space limitation? 4. Dependence on student volunteering
Opportunity 1. Feeding in Copenhagen trendiness: food culture, fashion, metropolitan 2. Improvement in social life/student life 3. Increasing inter-campus relation 4. People are more willing to attend events in the spring/summer	• Planning & marketing the event across all KU campuses to attract the most students • Ensure lots of diverse food stalls appealing to CPH food trends • Fashion show to appeal to CPH fashion trends • Leverage the existing international communities and contact them to get involved in the event • Hosting the event in May/June for likely good weather • Focus funding/ reimbursement on the appropriate food/performances	• Utilize the KU-net for marketing • Have posters across all the campuses to market the event • Diversify the event across campuses: (North Campus (Sports), South Campus (Food/Arts)) • Worst Case: Facilitate the contact between student volunteers and cultural stakeholders
Threats 1. Potential student dis-interest in participation 2. Funding unavailability from external investors 3. Dietary requirements 4. Casualties during the event (injuries from performances, fires)	• KU already has established risk assessments for big events run on campus that we can use. • Provide templates for food stalls to notify the ingredients. • Focus on funding from KU, specifically on the aspect that we are actively boosting the KU reputation	• Incentive for student volunteers to get involved (certificates / free food) • Write a specific risk assessment for our event • Have a technical rehearsal for the spaces to be used • Ensure that there is a first-aid kit/medical staff during the event

Table 4 – SWOT strategy development

5.1.4. Description of your considerations about concrete actions/activities resulting from the analysis that must be included in the project plan

1. Time of the event:
 - The event is to be hosted in early May as to not coincide with the KU festival whilst still enjoying late spring weather.
2. Funding:
 - Reach out to both external investors such as the Novo Nordisk Foundation as well as internal KU funds.
3. Marketing:
 - The Marketing plan must consider marketing across all the KU campuses. Utilising the online network and the screens across campuses as well as posing posters across campuses.
4. Volunteers:
 - Reach out to all the diverse cultures at the university to volunteer representing their culture.
 - Provide a capped reimbursement scheme for the materials needed to showcase culture.
 - Provide free food at the planning meetings for student volunteers as well as a certificate of volunteering upon completion.
5. Permits:
 - Request permits to host event on university grounds. This is coupled with getting the appropriate risk assessments completed through the university.
6. Event Prerequisites:
 - The two days leading up to the event, there will be “technical rehearsals” ensuring that all necessary technology associated with the event works.
 - All food stalls will be required to fill out and showcase a provided allergens form alongside their food.

5.2. Stakeholder analysis

5.2.1. Power/interest grid

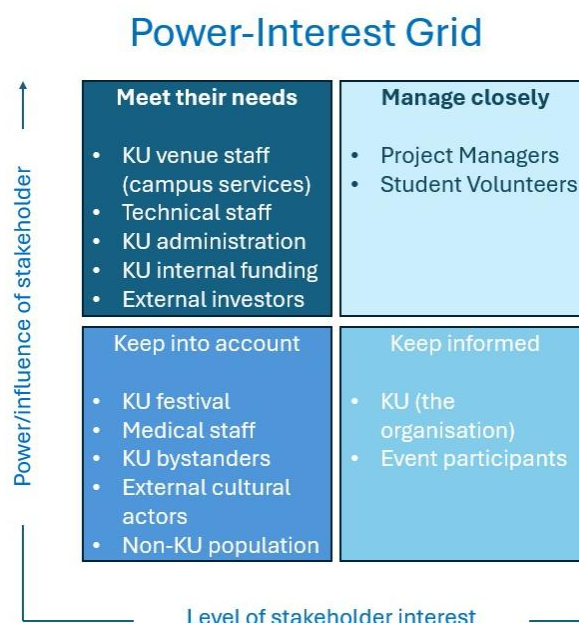


Figure 2 – Power/Interest grid

5.2.2. Stakeholder register¹:

Stakeholders in the project	Stakeholder's role in/contribution to the project	Power	Interest	Advantages or/and disadvantages of the project seen from the stakeholder's point of view	Possible strategies for engaging stakeholder
KU (organisation)	The event is run using the KU name and as such the KU reputation will be affected.	Low	High	A: • Reputation building • Improving student life/experience which could lead to improvement in performance D: • Potentially negatively impacting if project fails	Keep informed • Make sure that KU knows what the event is about and when it will be. • Do not need them to participate
Student and staff participants	There is no event without participants	Low	High	A: • Good experience • Cultural enrichment D: • Limited cultural exchange opportunity if event fails	Keep informed • Marketing of the event • Promote the sign ups
Student Volunteers	The project is run by student volunteers manning the booths and bringing different cultures	High	High	A: • Getting work experience • CV enhancement • Socialisation opportunity D: • Limited time towards studies	Manage Closely • Meet semi - regularly with check ins for key deliverables • Help make contacts when needed.
Project Manager	Facilitates and initiates the event and the volunteers	High	High	A: • Experience in planning the event • CV enhancement D: • Limited time towards studies • Ruined reputation if project fails	Manage closely • Regular meetings • Communication channels during event

¹ (Based on Fangel (2013): *Proaktiv projektledelse* Fangel Consulting as and Attrup & Olsson 2011: *Power i projekter og portefølje* Jurist- og Økonomforlaget)

KU Venue Staff (campus services)	Provide tables etc. needed for the event.	High	Low	A: - Get to ensure resources are available for event D: - Repairs in cases of damages	Keep satisfied - Inform them early enough - Open attendance to the event
Technical Staff	Helps with IT relevant for the event	High	Low	A: - Get to ensure resources are available for event D: - Damages to the technical instruments	Keep satisfied - Inform them early enough - Open attendance to the event
KU Administration	Providing the permission (permits) for the event.	High	Low	A: - Boosting KU's image D: - Overwhelming workload	Keep satisfied Early contact and approval of the event and the venue
KU Funding	Funds the event	High	Low	A: - Return on investment (reputation -wise) D: - No return on investment	Keep satisfied - Early contact regarding funding of event - Market the funding after the event (branding)
External Investors	Funds the event	High	Low	A: - Return on investment (reputation -wise) D: - No return on investment	Keep satisfied - Early contact regarding funding of eventing - Marketing of the investors after the event (branding)
KU Festival	They are a potential competitor for the event.	Low	Low	A: - Opportunity for increased attendance at their festival D: - Event is more successful than festival (attendance, ambience...)	Keep in to account - Find project managers for the festival and exchange strategies with them and keep them updated about our event - Help with marketing of the festival in our own event

					Possible avenues for collaboration with the festival on some events
Medical Staff	They would be needed on hand in case of injury	Low	Low	A: - Get to support in case of emergency D: - People getting injured	Keep in to account - Prepare a firstaid kit using their help - Keep them ready in case of a medical emergency
People at the venue not attending the event	These people might be affected by the noise / people that are attending the event during their lectures	Low	Low	A: - Participation in the event – opportunity for cultural experience D: - Disturbance due to the event	Keep in to account - Inform them of the event beforehand (via KU mail) - Ensure the event doesn't coincide with major exams/other academic activities
External cultural actors	These actors can bring additional cultural material helping the student volunteers	Low	Low	A: - Opportunity to make profit from selling services - Advertising for them D: - Opportunity cost of making money elsewhere - Service not appreciated	Provide general information - If they are interested -> are moved to high interest/low power - Possibility to do marketing for their brand/restaurant at KU-->new costumers

Table 5 – Stakeholder register/analysis

5.3. Complexity Analysis

	Complexity (1=low, 4=high)					Activity/strategy if needed	
Mission (project task)		1	2	3	4		
Is there a clear goal for the project?	A very clear single goal	X				No clear goals. Many different goals. Goals can change	To keep goal in mind – cultural exchange
Are all deliverables of the project known?	All deliverables are known		X			Only some of the deliverables (the major one) are known	We are dependent on the student volunteers to deliver the actual cultural experience. We will need to have check ins with them to ensure that this is fulfilled.
Is there a large number of deliverables ?	There only one or few deliverables and they are all known			X		There are many different deliverables – some unknown	As the event has several aspects there are many deliverables. We will need to ensure clear communication lines and deadlines for deliverables.
Is the use of resources known?	The use of resources is known and is not too big	X				The use of resources is big and unknown	Event space and facilities, volunteers and participants.
Is the timescale long?	The timescale is short (from few months to a year)	X				The timescale is long, and it is difficult to estimate how many years it will take	Planning, initiation and execution to be done in ≈ 8 months.
Does the project involve new technology?	The technology is well known	X				The project will develop new technology to meet the task	The project is an event. No new tech needed.
Has the project (or similar projects) been done before?	The project has been done before		X			The project has never been done before	Large scale events have been done but none in the cultural exchange space.

Are threats against the project known and predictable?	Threats are predictable		X			Threats are unpredictable and unknown threats maybe exists	We are aware of the risks but cannot for see if they will happen (weather, accidents, human error)
Organisation							
Is there a clear organisation ?	The organisation in and around the project is clear		X			The organisation of the project is not clear. Different organisations in different part of the project	There are clear groups with distinct responsibilities, but the organisation of the subcommittees is dependent on student volunteers. Need to be able to communicate with them.
Is the decision-making process in the project clear?	The decision-making process is clear			X		The decision-making process is not clear, many organisations and stakeholders are involved	The event is dependent on many different stakeholders / experts to be successful.
Will it be possible to have face-to-face meetings with all project team members?	All team members can meet. Contact is easy		X			Too many team members to meet. Geographical impossible to meet.	Geographically it is possible but there are many people involved so instead it may be prudent to have "sub-committee" meetings for different deliverables.
Delivery							
Does the project team understand the project management methodology?	All team members are familiar with methodology		X			Many team members and many who are unfamiliar with methodology.	The project team has clear framework that can be shared with project volunteers in due time.
Does the project need key experts?	No key experts are needed				X	Many different key experts are needed	The project is dependent on cultural and technical experts. Communication and check ins with these stakeholders will be of key importance.

Stakeholders						
Are stakeholders known?	All Stakeholders are known.		X		Some stakeholders are unknown. Stakeholders can change.	We expect some new stakeholders to be introduced during the initiation of the project.
Number of stakeholders	Few stakeholders			X	Many stakeholders – some unknown	The event caters to many people and affects an entire university. It will be important to inform each stakeholder in due time before the event.
Are the interests of stakeholders known?	Interests are known. Interests are homogeneous			X	Interests are unknown. Many different interests	Some interests are assumed and as such would need to be clarified in meetings with various stakeholders.
Is it easy to get in contact with stakeholders?	Stakeholders are local. Speak same language	X			Stakeholders live all over (global). Stakeholders do not speak same language	All stakeholders are in the CPH area and speak English!
Team						
Does the project involve multiple technical disciplines?	The project involves only one or few technical disciplines	X			The project involves multiple technical disciplines	The team will need to have skills in outreach and marketing.
Do project team members have same language	All project team members speak same language and are located at same place	X			Project team members speak many different language and are located all over the world	All team members will be in the CPH area and be able to meet in English.

Table 5 – Complexity analysis

Characterising management complexity:

Average complexity for the overall project is **2**: Most factors are well known with some room for unplanned events. Overall, it is a straightforward and realistic project to manage.

Challenges for the project management:

- Getting enough student volunteers and with oversight on their responsibilities.
- Managing the expectation of several stakeholders with different agendas.
- Communications with all the various stakeholders at the appropriate times.

Specific initiatives or strategies to handle challenges:

- Timely meetings with project stakeholders
- Creation of clear and concise marketing
- Decide on an incentive for student volunteers

Consequences:

- **Lack of Funding:** In case there is no funding from KU or external investors, the event will have to be self-funded by the student body or the event will not be able to be held. Furthermore, the event could be ticketed as to bring in a source of income to pay off the event.
- **Lack of cultural volunteers:** In the case of a lack of cultural volunteers there will be no showcase of the diverse cultures at the university. As such to ameliorate this, some of the funding can be allocated to pay cultural establishments to represent their cultures.
- **Lack of student volunteers:** In the case of a lack of student volunteers there will be a strain on the actual organisation of the event. As such, there can be funding put aside to pay for workers on the day of the event.
- **Lack of Student Interest:** In case of a lack of student interest the risk is that there is no one will attend the event.
- **No Permits from KU:** In case no permits are given by the university, other external locations can be scouted and paid for. Otherwise, the project will have no venue.

5.4. Communication plan

Target, audience	What information	Purpose, effect	Method of communication	When	Provider, responsible
KU (organisation)	Basic practical information regarding the event.	To ensure that KU want to attach their name and reputation to the event.	Email and/or short meeting	First meeting in the early phases (Sept) and then a follow up meeting 1 month before event	Project team/manager is responsible for planning these meetings.
Student and staff participants	Marketing material and sign-up forms to promote the event.	The purpose is to generate buzz around the event and get students involved.	- Physical marketing material: Posters, newsletters, KU net announcements - Social Media posts	1-2 months leading up to the event. Continuous posts around campuses.	Marketing team within the project team.
Student Volunteers	Information surrounding what type of cultural material will be showcased and how many people are in each team.	The project management team needs to know what cultures and activities will be showcased to facilitate.	Regular meetings throughout the initiation.	Bi-weekly/monthly in the 4 months leading up to the event.	PM plans the meeting, but the updates are coming from the student volunteers.
Project Manager	- Clear knowledge on project purpose and goal - Info on the stakeholders and their interest - Info on the risks around the project - Overall information about all components of project	It will help the project team to keep control over the organisation of the project.	N/A	Throughout the project	PM

KU Venue Staff (campus services)	Time and place of their intervention.	Ensure that the event has all the required facilities in a timely manner	- Email - Phone calls	1 or 2 months before intervention	PM
Technical Staff	Time and place of their intervention.	Ensure that the event has all the required facilities in a timely manner.	- Email - Phone calls	1 or 2 months before intervention	PM
KU Administration	- Time and days of the event - Number of people attending - Approved fire plan for setup of booths	Get the venue and event plan accepted, so core team can execute the event	Communication through mail	8 months prior to the event (November)*	The PM is responsible for the communication with the administration
KU Funding	What event funding is required for and why this event is worth that investment.	Getting money to execute the event to give money to the volunteers to showcase their cultures through food, art etc.	Email	8 months prior to the event (November)*	The PM
External Investors	What event we are asking funding to and why they should fund us.	Getting money to execute the event to give money to the volunteers to showcase their cultures through food, art etc.	Email	8 months prior to the event (November)*	The PM
KU Festival	Keep them generally informed about the event and exchange ideas on how to collaborate and improve in our events.	Possible collaboration, outreach leading to bigger audience, and networking leading to better opportunities	Emails and meetings	4 months before the event	Project managers and project coordinators

Medical Staff	- Keep them generally informed about the event. - Coordination about assembling a first-aid kit. - Constantly accessible during the event (especially in case of a medical emergency)	To avoid and minimise casualties	Calls, meetings and emails	1 month before the event	Project coordinators
People at the venue not attending the event	Inquire about the exam timings and other events happening during and around the time of our event. Also keep them generally informed about the event.	Avoid disturbance and conflicts with other academic and social events on campus	Email, calls	Participation survey email roughly 4 months ago, followed by signups and general correspondences starting a month ago.	Project coordinator and student volunteers
External cultural actors	If volunteers would like work together with an external, they can reach out	- Branding of the extractors business. - Showcase multicultural cultures in Copenhagen. Take work away from the volunteers.	Emails, meetings. KU can help facilitate student volunteers with external actors	After recruitment of volunteers, and when they know what they would like to showcase from their cultures	Student volunteers and KU (as a possible facilitator)

Table 6 – Communication plan

* Once the network diagram was completed, it was calculated through a backward pass that the project had to be initiated in September as the critical path was 9 months from the end of the project.

6. Project plan

6.1. Project objectives

- 1. Form a core team for the management and execution of the event by September 2025.
- 2. Obtain all the rightful administrative authorisation for the organisation of the event from the university authorities between end of November* and beginning of December 2025.
- 3. Secure total funding from external and internal contributors by the end of December 2025.
- 4. Recruit at least 50 volunteers, including supporting roles and culture representatives, by March 2026.
- 5. Design marketing strategy to attract at least 300 participants to the event 1 week before the event.
- 6. Provide recommendations, equipment, and resources, necessary for set-up for the cultural representatives up to 2 days before the event.
- 7. Aim for at least 70% of participants report a positive experience of event through post-event surveys.

*Once the network diagram was completed, it was calculated through a backward pass that the project had to be initiated in September as the critical path was 9 months from the end of the project.

6.2. Work Breakdown Structure and responsibilities

Work-Flow	Activities	Responsible Team	Duration of the activity	Allocation of staff
Theme 1	Complete the team building & role assignment			
1A	Identify the core team members	Project Manager	1 week	1 person
1B	Meet to define the roles and event idea.	Core Management Team	1 week	4 people
1C	Meet to develop a scheduled/plan for event.	Core Management Team	1 week	4 people
1D	Estimate the number of volunteers for each committee.	Core Management Team	1 week	1 person
1E	Book all meeting rooms	Core Management	1 week	1 person
Theme 2	Securing the necessary permits			
2A	Identify the appropriate KU authorisation for permits	Core Venue Team	1 week	1 person
2B	Contact the identified KU authorities	Core Venue Team	1 week	1 person
2C	Design requests for permit	Core Venue Team	1 week	1 person

2D	Submit permit request	Core Venue Team	4 weeks	1 person
2E	Contact the department in charge of venue	Core Venue Team	1 week	1 person
2F	Design request for venue	Core Venue Team	1 week	1 person
2G	Submit venue request	Core Venue Team	4 weeks	1 person
Theme 3	Securing funding for event			
3A	Identify potential funding sources for event.	Core Fund Team	2 weeks	1 person
3B	Identify process for funding request.	Core Fund Team	2 weeks	1 person
3C	Allocate funds for different activities	Core Fund Team	1 week	1 person
3D	Draw up/write a funding proposal for event.	Core Fund Team	2 weeks	1 person
3E	Meet funding partner(s) to present proposal.	Core Fund Team	4 weeks	1 person
Theme 4	Recruitment for volunteers			
4A	Research the distribution of existing cultural diversity at KU	Core Management Team	1 week	1 person
4B	Prepare a call for volunteers.	Core Management Team	1 week	1 person
4C	Send out the call for volunteers	Core Management Team	4 weeks	1 person
4D	Distribute volunteers amongst organisational committees and cultural committees (also cultural reps)	Core Management Team	1 week	1 person
Theme 5	Creation of cultural platform			
5A	Organise volunteer meetings – plan content of meeting (performance management) **	Primary: Core Management Team, Secondary: Core Volunteer Team	12 weeks	3 people
5B	Develop a form for specification of the cultural activities	Core Volunteer Team	1 weeks	1 person
5C	Send specification form out online to cultural representatives	Core Volunteer Team	3 weeks	1 people
5D	Update event schedule	Core Volunteer Team	1 week	3 people
5E	Identify external cultural contacts for the volunteers.	Core Volunteer Team	1 week	3 people
5F	Develop a reimbursement form.	Core Fund Team	1 week	1 person
5G	Send reimbursement form out online to cultural representatives	Core Fund Team	2 weeks	1 person

5H	Carry out the accounting for the reimbursement	Core Fund Team	1 week	1 person
5I	Reimburse the funds spent by the cultural representatives	Core Fund Team	1 weeks	1 person
Theme 6	Execution of marketing strategy			
6A	Create a marketing plan	Marketing Team	2 weeks	1 person
6B	Create an intuitive sign-up form for the event	Marketing Team	1 week	1 person
6C	Send out the sign-up form	Marketing Team	8 weeks	1 person
6D	Design the marketing material	Marketing Team	4 weeks	7 people
6E	Design posting schedule for the online marketing	Marketing Team	1 week	1 person
6F	Put up all the physical marketing material.	Marketing Team	1 week	4 people
6G	Publish online marketing material	Marketing Team	1 week	1 person
6H	Send out event reminders	Marketing Team	1 week	1 person
Theme 7	Supply and check-up of equipment for the event.			
7A	Setup booths at the event space	Core Venue Team	1 week	5 people
7B	Book the stages and sports facilities	Core Venue Team	1 week	1 person
7C	Setup stages	Core Venue Team	1 week	1 person
7D	Run a technical test for performers	Core Venue Team	1 week	1 person
7E	Run technical check-ups for booths.	Core Venue Team	1 week	1 person
7F	Breakdown of booths and clean up space.	Core Venue Team	1 week	5 people
Theme 8	Gathering of feedback			
8A	Create a post-event online survey	Marketing Team	1 week	1 person
8B	Publish online survey	Marketing Team	1 week	1 person
8C	Evaluate feedback survey	Core Management Team	1 week	4 people
8D	Present feedback survey to stakeholders	Core Management Team	1 week	4 people

Table 7 – Work Breakdown Structure

**** The meetings are not part of the critical pathway and as such can take place over a 12-week period throughout the project.**

6.3. Network diagram, milestones and critical path

Considering the granularity of the WBS, hence the number of activities, the network diagram was constructed by condensing some activities, according to their respective themes. The duration was calculated by adding up the individual durations of the key activities within the themes.

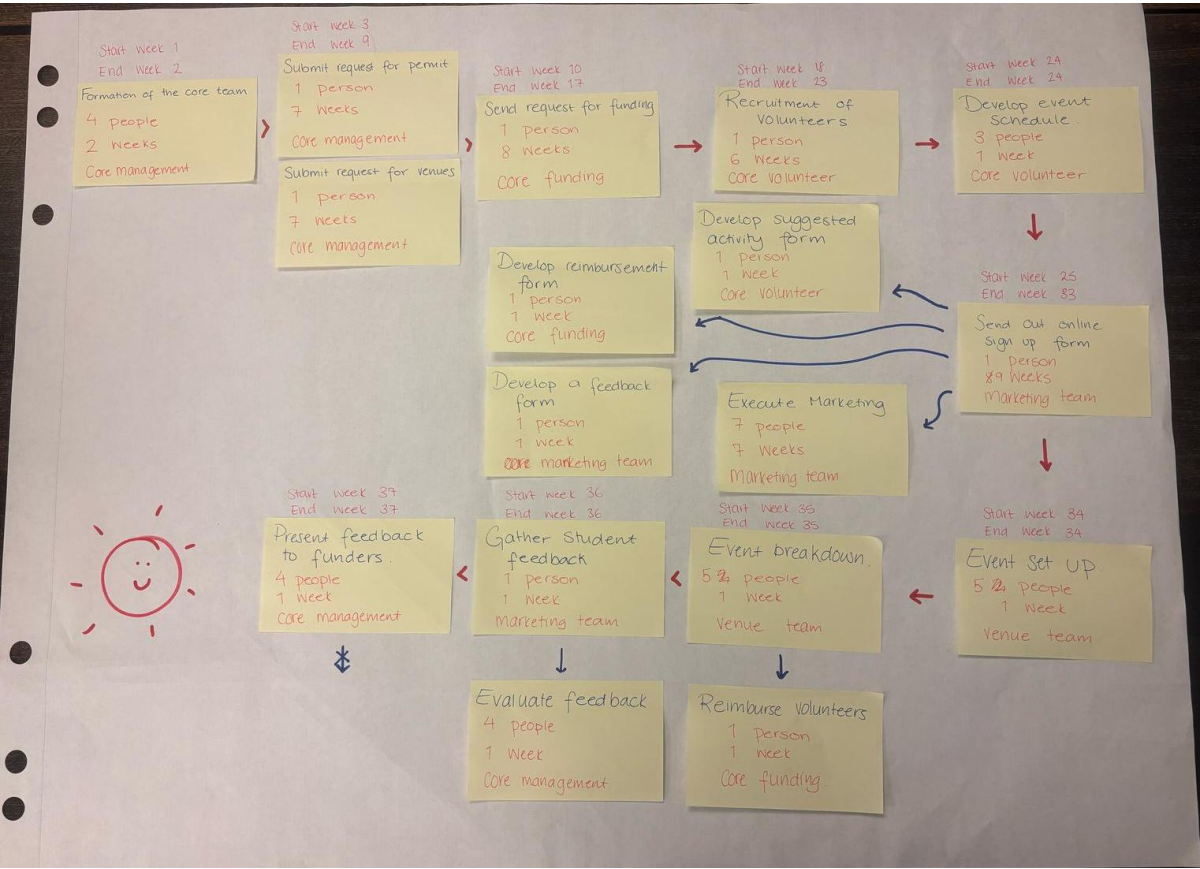


Image 1 – Original Network Diagram

To conclude, the critical path is indicated through the red arrows on the image and it is calculated to be **37 weeks**.

6.4. Schedule (e.g. Gantt)

Project title

Project start date

Project end date

Project Plan for Cultural Exchange Event

Monday, 2nd September 2025

Friday, 29th May 2026

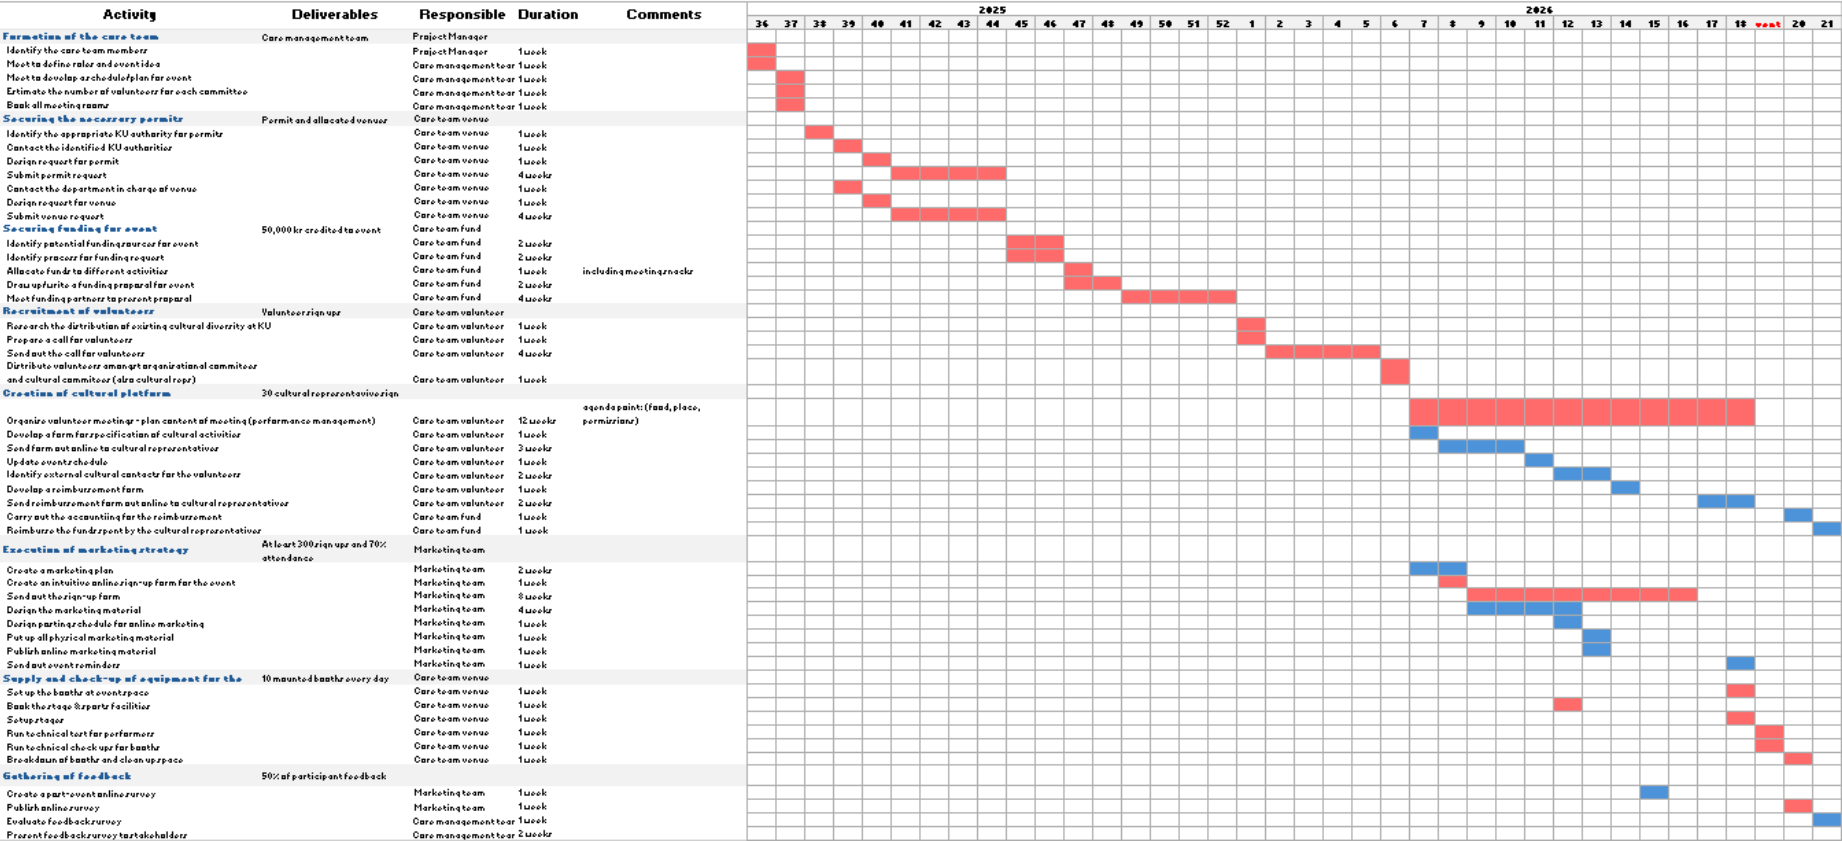


Figure 3 – Original Gantt Chart

6.5. Budget and cost-baseline

Task	Work-week [h]	Duration [weeks]	No of people	Cost [h] (effort)	Duration of task in each 5-week interval [week]								Cost of task in each interval [h]							
					1 to 5	6 to 10	11 to 15	16 to 20	21 to 25	26 to 30	31 to 35	36 to 40	1 to 5	6 to 10	11 to 15	16 to 20	21 to 25	26 to 30	31 to 35	36 to 40
Formation of the core team	40	2	4	320	2								320	0	0	0	0	0	0	0
Submit request for permit	40	7	1	280	3	4							120	160	0	0	0	0	0	0
Submit request for venue	40	7	1	280	3	4							120	160	0	0	0	0	0	0
Send request for funding	40	8	1	320		1	5	2					0	40	200	80	0	0	0	0
Recruitment of volunteers	40	6	1	240				3	3				0	0	0	120	120	0	0	0
Develop event schedule	40	1	3	120					1				0	0	0	0	120	0	0	0
Send out the online sign-up form	40	9	1	360					1	5	3		0	0	0	0	40	200	120	0
Event Setup	40	1	5	200							1		0	0	0	0	0	0	200	0
Event Breakdown	40	1	5	200							1		0	0	0	0	0	0	200	0
Gather student feedback	40	1	1	40								1	0	0	0	0	0	0	0	40
Present feedback to funders	40	1	4	160								1	0	0	0	0	0	0	0	160
	40			0									0	0	0	0	0	0	0	0
Develop suggested activity form	40	1	1	40					1				0	0	0	0	40	0	0	0
Develop reimbursement form	40	1	1	40					1				0	0	0	0	40	0	0	0
Develop a feedback form	40	1	1	40					1				0	0	0	0	40	0	0	0
Execute marketing	40	7	7	1960					1	5	1		0	0	0	0	280	1400	280	0
	40			0									0	0	0	0	0	0	0	0
Reimburse volunteers	40	1	1	40							1		0	0	0	0	0	0	40	0
	40			0									0	0	0	0	0	0	0	0
Evaluate feedback	40	1	4	160							1		0	0	0	0	0	0	160	0
	40			0									0	0	0	0	0	0	0	0
	40			0									0	0	0	0	0	0	0	0
	40			0									0	0	0	0	0	0	0	0
	40			0									0	0	0	0	0	0	0	0
	40			0									0	0	0	0	0	0	0	0
Budget at completion (BAC):				4800	Cost for each interval								560	360	200	200	680	1600	1000	200
					Accumulated cost								560	920	1120	1320	2000	3600	4600	4800

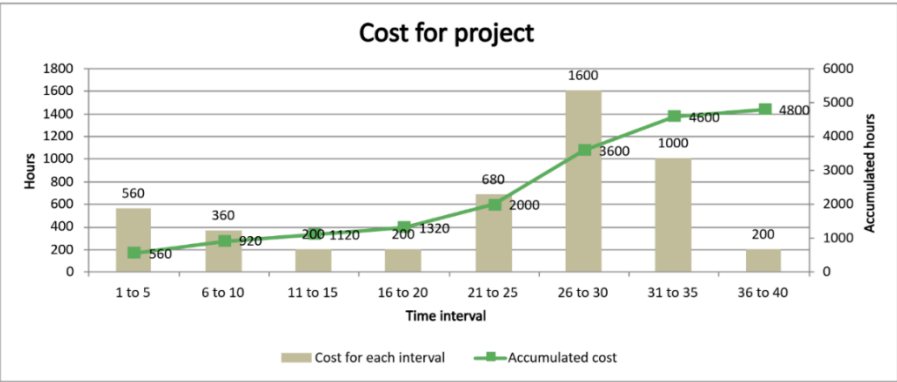


Table 8 – Budget and cost baseline

6.6 Risk analysis

				Before response 1 (low) – 4 (very high)				After response 1 (low) – 4 (very high)	
	Trigger	Risk	Impact on project	Prob.	Imp.	Type of Response	Response	Prob.	Imp
1	Insufficient incentive to join as a volunteer for the event	No volunteers sign up for the event.	There will be no student volunteers for the event or as cultural representatives	3	4	Mitigate	At a decided time, change the volunteering position to a paid position. Account for this in budget allocation.	2	4
2	All the meeting rooms of appropriate size are already booked.	It is not possible to host in person meetings with volunteers to inform them regarding updates for the event.	The volunteers are uninformed and do not know what is expected of them for the organisation of the event.	2	4	Avoid	Host all meetings online (teams/zoom etc.) whereby all attendees can join from home.	0	0
3	No attendee fills out a feedback form.	The project does not receive at least 50% feedback from the event.	Impact of the event is not evaluated from the student perspective and may not continue to run in the future.	2	2	Accept and be proactive	Wait and see. Further make an internal assessment of the event.	2	1
4	Students are not signing up via the posted marketing material.	The organisation team does not receive an accurate approximation of attendees for the event.	Either more or less people than expected (300) show up.	3	2	Accept	Keep planning the event for the expectant 300 attendees as set up in goal.	3	2

Table 9 – Risk Analysis

Assessments before and after risk management:

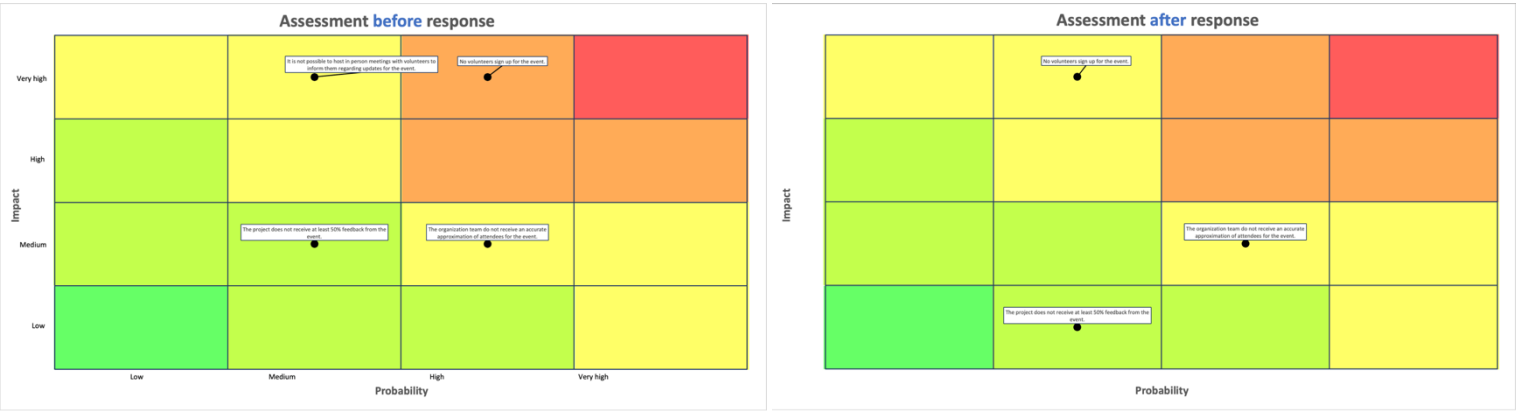


Figure 4 – Before and after of risk management

Amendments to WBS after risk management:

Work-Flow	Activities	Responsible Team	Duration of the activity	Allocation of staff
Theme 1	Complete the team building & role assignment			
1E	Book all meeting rooms	Core Management	1 week	1 person
1E	Send online meeting invitations	Core Management Team	1 week	1 person
Theme 4	Recruitment for volunteers			
4A	Research the distribution of existing cultural diversity at KU	Core Management Team	1 week	1 person
4B	Prepare a call for cultural volunteers.	Core Management Team	1 week	1 person
4C	Prepare a job offer for event support workers	Core Management Team	1 week	1 person
4D	Send out the call for volunteers & workers	Core Management Team	4 weeks	1 person
4E	Distribute volunteers amongst organisational committees and cultural committees (also cultural reps)	Core Management Team	1 week	1 person
Theme 8	Gathering of feedback			
8A	Create a post-event online survey	Marketing Team	1 week	1 person
8B	Prepare internal assessment of the event	Core Management Team	1 week	1 person
8C	Publish online survey	Marketing Team	1 week	1 person
8D	Complete internal assessment of the event	Core Management Team	1 week	1 person
8E	Evaluate feedback survey	Core Management Team	1 week	4 people
8F	Write a conclusion of internal assessment	Core Management Team	1 week	1 person
8G	Present feedback survey to stakeholders	Core Management Team	1 week	4 people

Table 10 – Amended WBS after risk management

Updated Network Diagram after risk management:

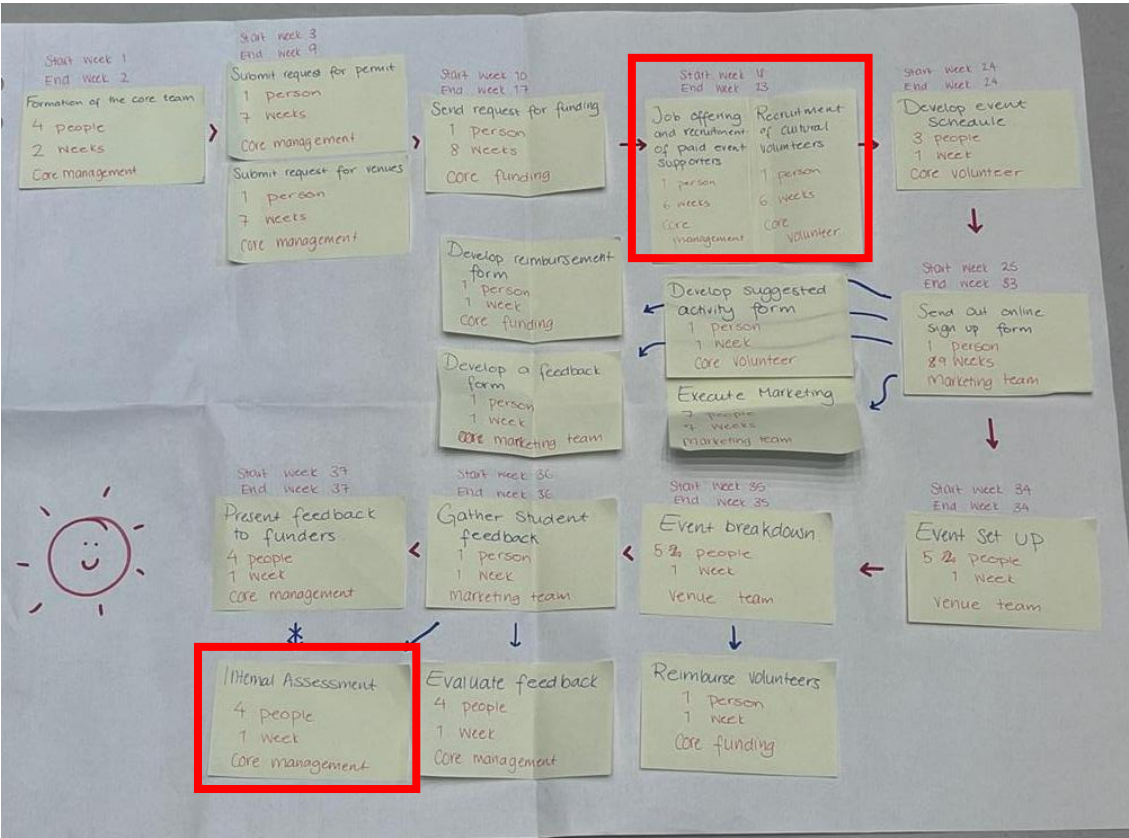


Image 2 – Amended Network Diagram

Project title	Project Plan for Cultural Exchange Event
Project start date	Monday, 2nd September 2025
Project end date	Friday, 8th May 2026

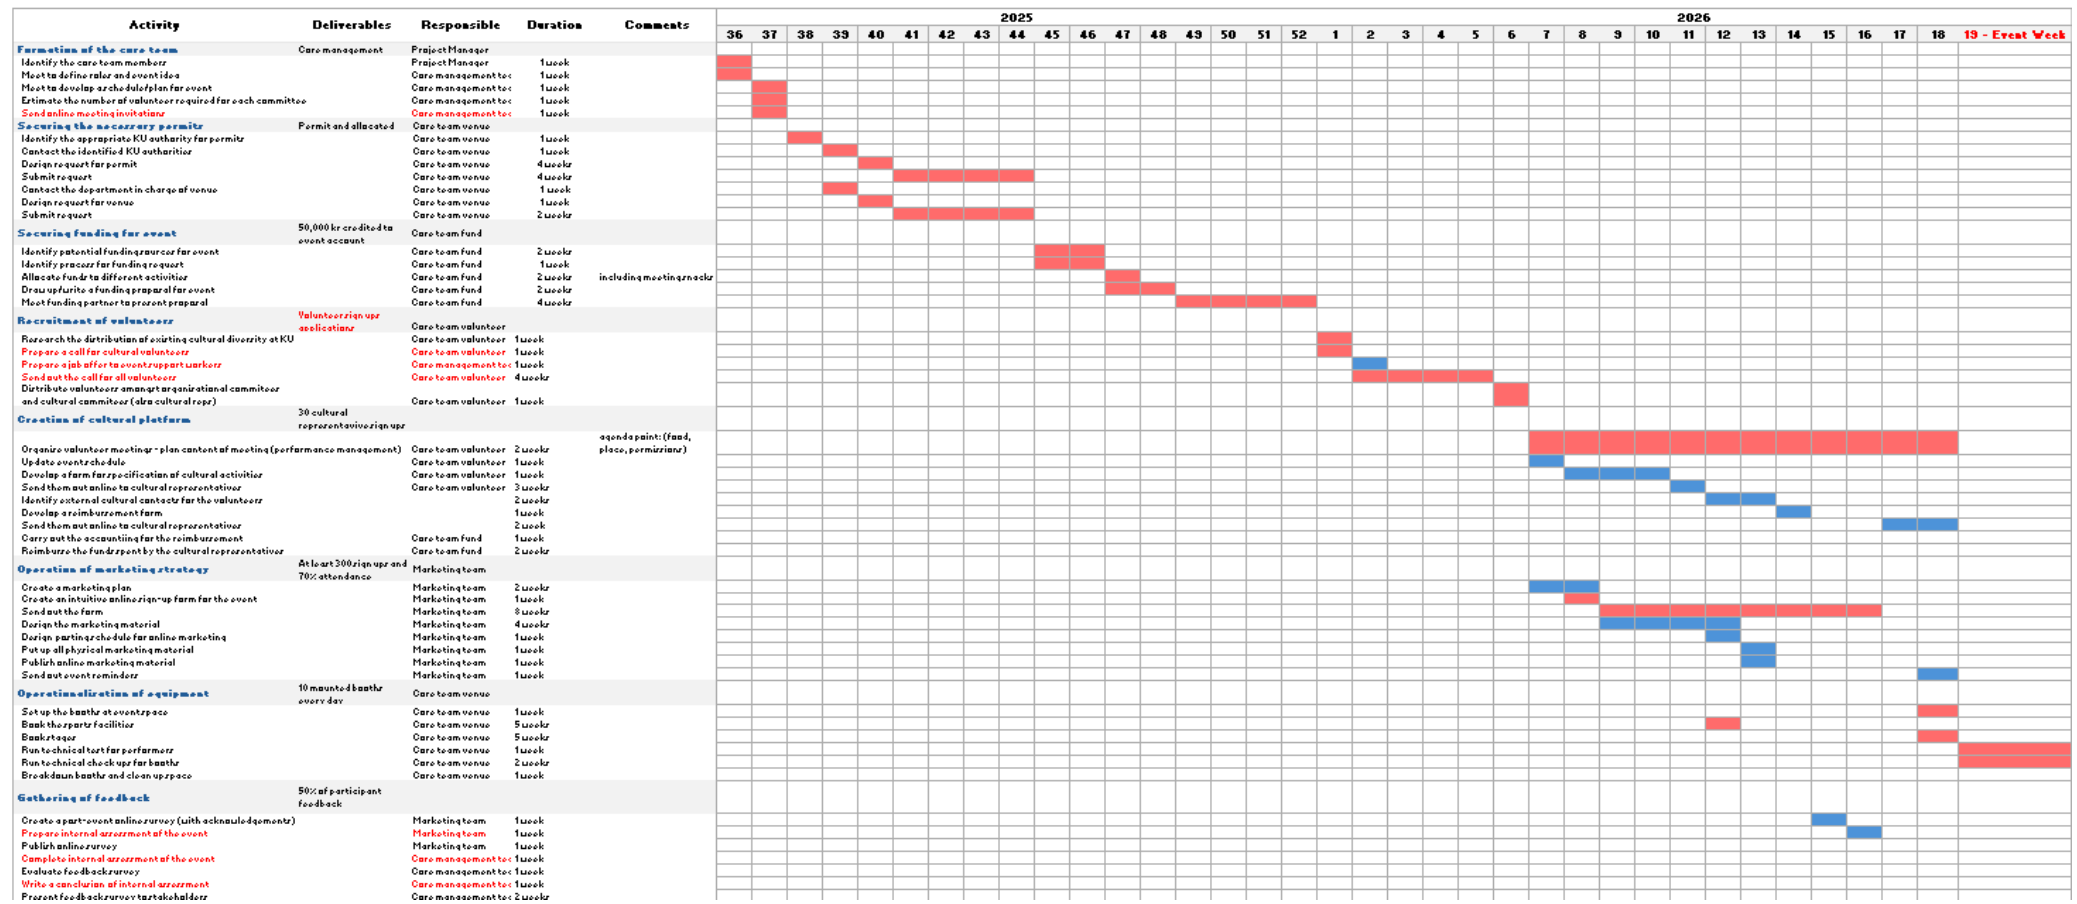


Figure 4 – Amended Gantt Chart

7. Learning reflection

7.1. Collective reflections on your working and learning process

Through the forming phase, there was a relaxed vibe/atmosphere in the group, where we got to know each other. Before meeting we had taken the JTI tests, which became a part of our ice breaker and helped us to understand each other better from the jump. We did an icebreaking game and grabbed a cup of coffee together the first day. It created the setting to talk about our goals for this course, and the setting to make the ground rules for the team's collaboration. In the first round, **Dagmar** was the PM. She prioritised actively listening to the team members, participatory decision making, and making the best use of their abilities in task execution.

In the second round, with **Om** as the PM, the knowledge of the JTI test, led the task delegation process. In other words, he ensured the tasks matched the personalities/work preferences of each group member. The format and structure setup by Dagmar was carried forward and provided a good ground base to build upon. The communication mediums were used more extensively, and an attempt was made to delegate responsibilities such that no one felt the pressure of it, while also providing a learning opportunity to grow the skills that each team member felt they lacked.

Extract from group logbook (04/03)

*"At the end of week 4, during the feedback sessions, we had time to discuss Om's performance as PM. This led us to a reflection on the interaction between the different personalities existing in the team. Specifically, we realised that there was a tendency sometimes for the other teammates (more often the extroverted types, but not only) to forget to allow the PM to initiate the activities and structure them, even though we had already established it in the ground rules. Hence, we decided that this week (the one for this log), we would review the ground rules before the start of the session so that we were all aligned on our work approach. As PM, I led the discussion and tried to ensure that all opinions were expressed, then we updated the ground rules point by point. I appreciated that reflection and action because it reflected how serious we are taking this learning opportunity, and it reflects something that was said in the beginning of the course which was: **"We do not learn from experience... We learn from reflecting on experience"** (John Dewey); and that is what really happened there."*

In the third round, **Stéphanie** was the PM. The workload was heavier and the importance of finalising the document became more apparent as this was the last phase of the project. The work approach employed by the PM different as she had to have a good overview of all sections of the PM-file and ensure an execution of all instructions. She prioritised attention to detail (which is aligned with her personality), document quality and accessibility, and delegation led by observed work approach and learning objectives of team members.

While **Smilla**, did not have a PM term, she found that the JTI the personality tests were useful in providing a framework and common vocabulary to communicate how she works and interacts within a group setting.

The norming phase was quite efficiently handled both with respect to task delegation and the management of time. Every topic of planning was approached by a brief introduction and a format laid out by the PM, followed by methodical opinion gathering and assessment by each team member. When short of time or energy, the PM delegated the tasks to the team members to get them completed on their own time or alone. These tasks were later collectively reflected upon, and appropriate changes or addition were incorporated. A combination of both these methods helped us to perform efficiently while also allowing everyone the personal space to work according to their own styles and at their own leisure. The bouts of intense discussions were often broken up by moments of laughter and jokes, which held the team morale high and boosted energy in the work. A couple of group sessions also offered homemade delicacies to keep our stomachs satisfied during the work. These little actions increased the bonding in the group and brought us closer together as a team. We often alternated between the waterfall and agile models of working and hence could provide flexibility of not knowing certain aspects of the project beforehand, while also incorporating several iterations of improvements to fill out the missing information. This method was especially handy to identify key pieces of quantitative data such as the date of the event, the number of team members and role profiles needed.

The biggest learning as a group was the confidence that we gained about being comfortable to work with people of different personalities. Since this aspect was very explicitly highlighted through the JTI results right at the beginning of the course and group formation, it was great to witness the level of bonding that could be created between such different personality types.

7.2. Evaluation of ground rules, goals, ambitions and leadership formulated in chap. 2^{11/2}

Name of PM: Dagmar

PM-Period: 4/2 - 13/2

Week 1 or 2 of the PM-period: 2

SUBJECT	ISSUES – POSITIVE AS WELL AS NEGATIVE	REFLECTIONS & LESSONS LEARNED	ACTION TO BE TAKEN (IF NECESSARY)	RESPONSIBLE
Feedback to the Project Manager.				
Communication in the team	It was clear and transparent. Everyone in the team was made comfortable to voice their opinions.	Crisp and effective communication tactics led to efficient time management and left no space for misunderstandings amongst the team members.	Maintaining effective communication strategies throughout the planning phase	All future PMs
Social life in the team	Very positive and Dagmar was able to get the team well incorporated through team building and social elements. Maybe one aspect to work on is to make sure that social chats do not take over too much	Dagmar was presented with a very chatty and socially curious team – which is always a challenge to manage the balance between work and social aspects. As this was the forming stage Dagmar successfully was able to get the team comfortable working together.	Actions for the next PM would be to follow the stages of team formation (storming/norming/performing) with team dynamics and balancing the social and working dynamic within the group.	All future PMs
Use of Ground Rules	The discussion around the ground rules was excellent and made sure that we were all on the same page. The implementation of the ground rules hasn't been super stringent as the team is still getting comfortable.	They are so new, so it seems to have been hard to implement them immediately as a PM within the group.	Maybe to remind the team regarding the ground rules before the meetings.	All future PMs to remind but team members to implement
Organising the work in the team	The tasks were delegated according to the team members' interests and expertise. The team's proactive efforts helped Dagmar to provide structure during the initiation phase.	Dagmar methodically prepared the time schedules for implementing the procedure outlined in the PM file. The schedules were created well before the deadlines to allow ample space for the team members to execute them at their convenience.	The actions can be planned even more in advance to facilitate better convenience for the team members to execute their contributions to the initiation phase.	All future PMs

Leading meetings	Dagmar communicated with the team that she needed help with structure of the meetings. This was showcased in some of the discussions taking too much time or getting in too gritty detail.	Dagmar was able to turn this around and implement a timekeeper and a secretary to record the minutes to ensure that the deliverables for each day were met. In cases where time did run out, “homework” was also set forth and respected	Future PMs should also implement a timekeeper and a secretary to keep the team on time and schedule with regards to deliverables.	All future PMs
------------------	--	---	---	----------------

Reflections on the collaboration in team				
Collaboration in the team	Overall, it was fluid and dynamic. At times, there were opposing points of view which could have been handled more objectively.	Collaborative effort takes time but yields in an outcome that is optimally suitable for all the team members. There are chances of the loss of democratisation of the process due to the differences in the personalities of the team members.	The team members assess their personality traits and try to deliberately compensate for their uneven contributions to the group collaboration.	All team members
Internal communication	We have two main channels of communication – WhatsApp and OneDrive. Both platforms good for collaborative work.	We have a lot of files that we need to understand more how to work on collaboratively and need to streamline how this is done.	Continue the organisation and understanding of where files belong and what should be worked on for the next meeting.	The respective PMs
Roles in the team (do you fill out the necessary roles?)	These are still being understood. At times there have been clashes of personality types resulting in extended discussions.	We have understood the theory of each personality type and how they fit in each role but need to see practically how they will develop.	More clarity in what each member should be doing with delegated tasks	Respective PM to delegate roles and for members to respect those roles
Meeting behaviour	Very casual meetings mixing the social and the professional.	We run the risk of working overtime if we do not concentrate our efforts on tasks at hand.	Sticking to the agenda and designated times as set out by the PM	Team
Respect of Ground Rules	This period the ground rules were established. More time needs to be put into the implementation and practice of them.	We are still getting comfortable with our ground rules and how they are being put in practice.	Implementing the ground rules further.	All team members
Reflections on tools you have worked with.				

What roles have the introduced tools in the last week played in the development of your project?	Ground Rules – positive to have the discussion regarding the statements. JTI Test – super interesting to understand the personality dynamics and how true they are for different individuals. The PM File	It helps structure the meetings by having a separate secretary making the logbook during the meeting and another one keeping an eye on time, so we can stay on schedule.	We could get more efficient in the planning of a project by having a clear structure.	PM (and the rest of the team is responsible too)
Are the tools useful?	The ground rules have provided a foundation for mutual understanding which is helpful. The JTI test really helped understand where everyone can shine and what goals each individual should set. The PM file is a helpful rubric to formulate and actuate the teams' thoughts.	The ground rules allowed for non-discriminatory baselines to build mutualistic relationships between the team members. The JTI test was helpful in assessing our own personalities as well as those of our teammates, thereby providing an open and safe space for symbiotic dialogue amongst the team members.	Spend less time on the reflection table	All PM members

Name of PM: Om

PM-Period: 14/2 – 27/2

Week 1 or 2 of the PM-period: Week 2

SUBJECT	ISSUES – POSITIVE AS WELL AS NEGATIVE	REFLECTIONS & LESSONS LEARNED	ACTION TO BE TAKEN (IF NECESSARY)	RESPONSIBLE
Feedback to the Project Manager.				
Communication in the team	The communication outside of class was very clear even when PM was ill so that the team could continue the work. Communication on the schedule was quite clear hence we always had a reference point for what we had to do for weekly in advance.	The WhatsApp group is good to keep each other in the loop regarding lateness/illness. Also, OneDrive is useful for collaborative work	Keep the communication channels open	All of the team
Social life in the team	Nothing has really changed here!	N/A	N/A	N/A
Use of Ground Rules	The PM (sometimes due to unavailability) was unsure of taking decisions as outlined in our ground rules. Considering his associated-personality type, he would need to be reminded sometimes by other members to take the lead/responsibility otherwise he would let the others do it.	We still need to work on implementing the ground rules properly in terms of decision making. It is important that other team members remain aware of the ground rules and personality types of each other to push them to step up when they need to such that they also learn from the experience.	Reminding each other of the ground rules – maybe having a refresher session	The team as a whole
Organising the work in the team	Got better through the days, having some good ideas for organising our analysis and working efficiently. He was a bit hesitant at times to assign tasks. Some organisation methods could have been more efficient.	Sometimes there was a lot of discussion on smaller details that could take over the actual work and a lot of time was spent on this. That took some energy out of the team when it came to do the actual work afterwards. Propositions for how to work could be made and agreed upon in the beginning, but we'd end up going back to it in the end.	Do not immediately shut down propositions. It is important to have quick/thorough thought and consideration about them before shutting different propositions before down.	PM

Leading meetings	PM was eager to lead which was positive but sometimes struggled with taking charge	The team needs to be able to let go and let the PM lead the sessions more independently.	Utilise the Ground Rules and respect each other's authority in the meetings.	The team is responsible for ensuring each PM gets their space to lead.
Other	A bit of confusion sometimes with what we were supposed to work on, where it took a long time to get started on a topic, where we were just sad and waited.	Working on clearer communication, especially when people or not really aligned, could be working on, by checking on members' thoughts and that we all understand what is going to happen. Clearer delegation of rules at the start of the days by listening to team members, to better utilise the team's expertise.	The PM should maybe have all the templates ready for each session so that we can get started immediately on all the work during the class sessions.	The PM is responsible for the creation of the templates to be filled in and clear time allocations.

Reflections on the collaboration in team				
Collaboration in the team	The collaboration was quite good. The team discussed the decisions together. In case of a lack of time, the tasks were completed individually and then reviewed together. The flow of discussion was very natural, and the qualities lacked by some were completed very well by others.	Some members had to be consciously pushed to contribute more while others had to be restrained in their communication.	The PM can more consciously be more decisive and forthcoming, while the others can be consciously less bearing on the decision-making for the group.	Everyone in the team
Internal communication	WhatsApp & OneDrive are useful tools here to ensure that we are not missing out on any information	Keep using them! The PM could have been clearer about his leading strategies in the group.	If needed: Structure the folders a bit more and clarify who is moving various chapters into the overall PM file.	The PM can delegate this task.
Roles in the team (do you fill out the necessary roles?)	This could have been more clearly defined at the beginning of the day.	I could become better by having maybe 5 min in the beginning of the meeting checking in and discussing what we should do and delegating what is needed.	Clear agenda, ask who would like to do what and if the team has any ideas to improve the way we go around our project work.	The PM can delegate tasks

Meeting behaviour	We are all very chatty and want to get involved – but this needs to be managed overall so that the PM can lead and organise the team	We often waste time because we get into details or derailed during meetings.	Have a clear agenda for meetings and clear action points for each meeting. Ensure to have meeting minutes completed by the end of each meeting.	The entire team. PM (meeting minutes)
Respect of Ground Rules	The team has potentially forgotten some of the ground rules (not massively but in small points)	The result is that there is conflicting planning or ideas or discussions that last too long without PM involvement.	Good to have a refresher of the ground rules so that we are all on the same page.	The entire team.
Reflections on tools you have worked with.				
What roles have the introduced tools in the last week played in the development of your project?	Project Charter / SWOT / Stakeholder Analysis / Complexity Analysis / Communications Plan	There is a lot of structural aspects and both internal and external factors that need to be considered when planning our event	No action now as all aspects have been filled in!	N/A
Are the tools useful?	These have overall been very useful as they have provided structure to the PM document and the project overall has more structure and substance	As a team we need to be timelier in our fulfillment of each part.	Potentially have shorter discussion sessions and then work on parts individually to save time and effort.	The PM

Name of PM: Stéphanie

PM-Period: 03/03 – 13/03

Week 1 or 2 of the PM-period: 2

SUBJECT	ISSUES – POSITIVE AS WELL AS NEGATIVE	REFLECTIONS & LESSONS LEARNED	ACTION TO BE TAKEN (IF NECESSARY)	RESPONSIBLE
Feedback to the Project Manager.				
Communication in the team	Has been very detailed regarding the tasks we had to make, with a lot of information. Showed in general a good overview of our tasks that needed to get done. The PM also gave sufficient opportunity for every team member to voice their opinions.	The instruction could have been made more simplified in their description, where the team members sometimes got a bit lost in a lot of information instead of focusing on the biggest main things to do and not get lost in smaller details, where it could be a bit difficult as the receiver to understand what needed to be done and what was the most important.	Acceptance of that people work in different ways and can have different standards and perseverance of when a task is done.	All
Social life in the team	We had a very good and cosy vibe in the team	N/A	N/A	All
Use of Ground Rules	Went through the ground rules a second time to make the member aware of how we can be better at managing our time.	It is useful to go through the ground rules to ensure all members are on the same page.	Increase awareness about the hierarchy of power in the team	All
Organising the work in the team	Very detailed regarding which tasks needed to be done and how they should be done. Showed a lot of knowledge but could become better at letting go and allowing people to work in a different way, than what the PM prefer. Very clear breakdown of action points which translated into clear delegated tasks. The PM also showed originality and critical thought in organising the work contents very well.	Very good with structure and awareness for details regarding the plan. Could work on a looser approach allowing people to work in their own way. PM was eager to listen to the team members, when we needed to move on from an activity or maybe make some changes in our analyses. Could also reflect on not overcomplicate some tasks, so we can work efficient and prioritising the work, as not all tasks are equally important, also with stuff that we had forgot to do in the earlier PM periods. There it could have been nice to let go and work around instead of trying to recreate aspects, that might not be necessary timewise.	N/A	PM

Leading meetings	Very thorough and showed a high standard for the projects content. They also had a high level of motivation to take responsibility and delegate tasks.	Made the team working harder for getting a high standard in the project. In certain situations, they could have been more decisive.	NA	PM
------------------	--	---	----	----

Reflections on the collaboration in team				
Collaboration in the team	We had a good collaboration and was good at speaking out loud, when we needed to adjust on our work.	While everyone was trying, the PM could have taken charge more while the other natural leaders of the group could have let go off their control a bit more.	We can try to build more self-awareness to balance the roles in the team.	All
Internal communication	The communication (both offline as well as online) was quite clear and transparent, leading to minimal misunderstandings amongst the team members.	The team members can work with each other despite a difference in their personalities and backgrounds.	NA	All
Roles in the team (do you fill out the necessary roles?)	There was good general self-awareness about our own roles in the team. However, at times, it could have been clearer, where not everyone in the group had something to do. This could have been used more efficient.	It felt easier to work with the roles that were complimentary to each team member's personality.	Try to play to your strengths.	All
Meeting behavior	The team members were very accommodative of each others' needs and tried to be friendly despite their personal problems.	Being considerate to other team members goes a long way in building trust and safe spaces for communication amongst the team members.	NA	All
Respect of Ground Rules	Most ground rules were followed well.	It was helpful to have the rules in the long term to find a common ground for communication and understanding.	NA	All

Reflections on tools you have worked with.				
What roles have the introduced tools in the last week played in the development of your project?	They have provided structure on how to think and practically perform different aspects of the project: WBS, network diagram, Gantt chart, Cost baseline chart.	Frameworks are good and helpful in thinking about projects and	While the tools could be quite repetitive – we also do understand that the purpose was to give the students the experience to work with them. In the professional context, we may not use them all, just select the most appropriate, hence that is something to keep in mind.	PM
Are the tools useful?	Very good to get an overview and to make a nice visual for how to make the project come alive.	Helpful the team members to be critically thoughtful and organised.	NA	All
